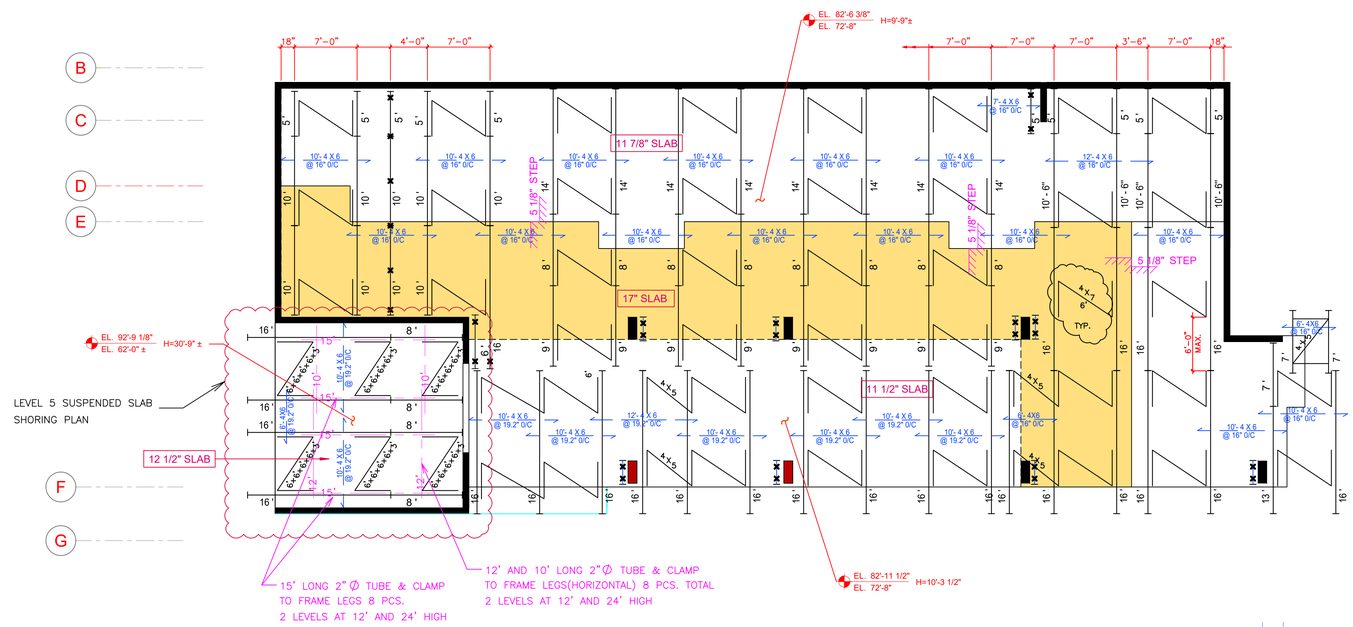

LEVEL 4 SUSPENDED SLAB SHORING PLAN : SCALE 1/8"=1'-0"

11"1/2 DEEP SLAB TYPICAL U.N.O. (194 P.S.F.)

FRAMES TO BE 6'-0" HIGH X 4'-0" WIDE H. DUTY (10K/LEG) WITH 7' BRACING TYP. U.N.O.

NO SHORE IS REQUIRED UNDER SLAB TYP. UNLESS SHOWN OR MARKED AS "X" FOR #2 POST SHORE TYP.(SEE PLAN FOR LOCATION).

PLYWOOD TO BE MIN. 3/4" D. FIR #1 OR BETTER.

FOR GENERAL NOTES AND TYPICAL DETAILS SEE DRAWING F-1.

INSPECTION IS REQUIRED BY UNDERSIGNED P. ENG. PRIOR TO POURING CONCRETE. (48 HOURS NOTICE PLEASE).

NOTES :

THIS DRAWING SHALL BE READ IN CONJUNCTION WITH ARCHITECTURAL AND STRUCTURAL DRAWINGS.

CONTRACTOR TO CHECK AND CONFIRM ALL DIMENSIONS & ELEVATIONS PRIOR TO SHIPMENT OF EQUIPMENT.

RESHORING DIAGRAM:

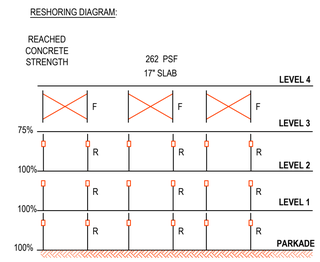

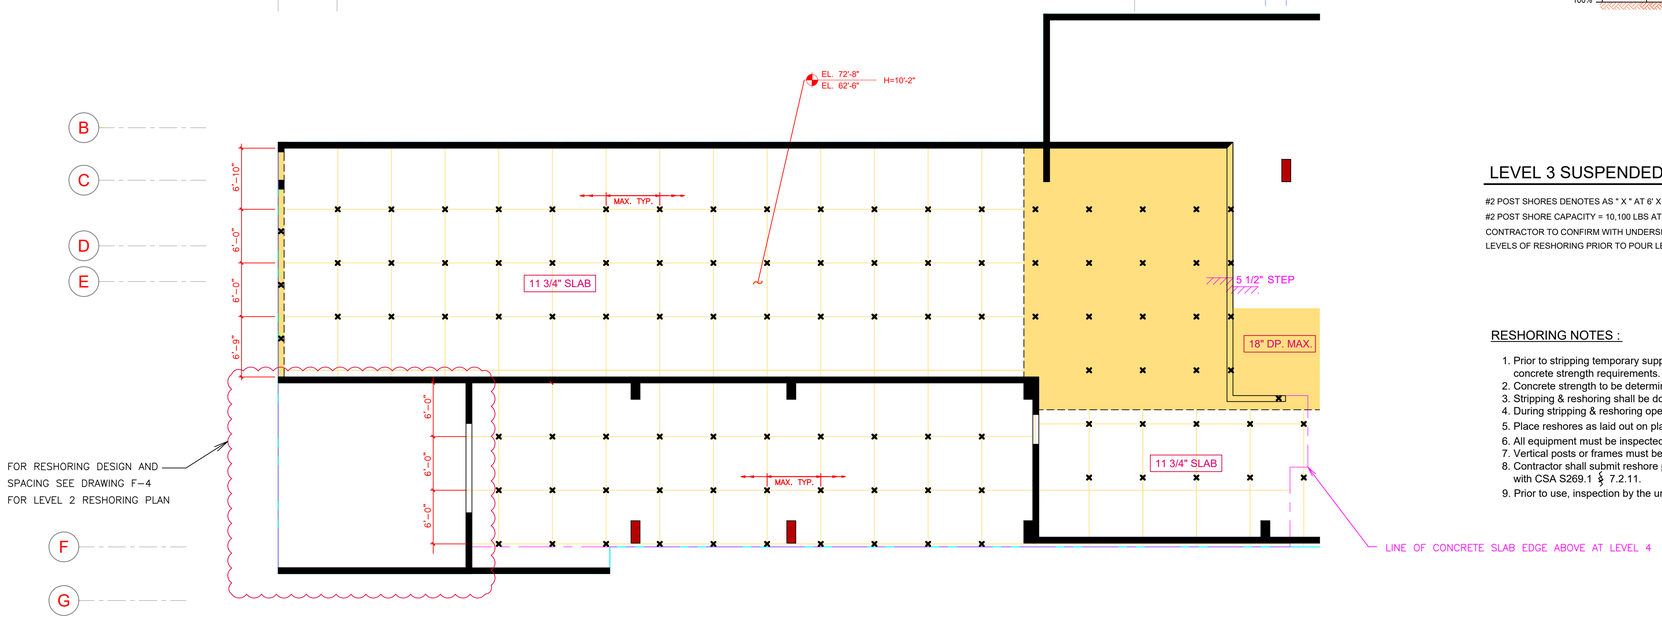

LEVEL 3 SUSPENDED SLAB RESHORING PLAN: SCALE 1/8"=1'-0"

#2 POST SHORES DENOTES AS " X " AT 6' X 6' GRID MAX. TYP. U.N.O.

#2 POST SHORE CAPACITY = 10,100 LBS AT 9' HIGH EXTENSION

CONTRACTOR TO CONFIRM WITH UNDERSIGNED P. ENG. FOR MINIMUM LEVELS OF RESHORING PRIOR TO POUR LEVEL 4 AND 5 CONCRETE.

RESHORING NOTES :

1. Prior to stripping temporary support, contractor to confirm with structural engineer minimum concrete strength requirements. Concrete strength shall not be less than 70 % of design strength .
2. Concrete strength to be determined by field cured cylinders.
3. Stripping & reshoring shall be done on same day . Do not leave unreshored slab overnight.
4. During stripping & reshoring operation, at least one complete bay to be cleared before any reshores are installed.
5. Place reshores as laid out on plan, denoted by ' X ' for # 2 post shore TYP.
6. All equipment must be inspected by contractor prior to use. Bent or damaged equipment should not be used.
7. Vertical posts or frames must be within 1/2 " of plumb and must be checked prior to concrete placement .
8. Contractor shall submit reshore plans to designer of the permanent structure for acceptance in accordance with CSA S269.1 § 7.2.11.
9. Prior to use, inspection by the undersigned P. Eng. is required . (48 hrs. notice , please).

GREUTER ENGINEERING LTD.
EGBC PERMIT NO. 1002364
FILE: GE-2488-4

PROFESSIONAL ENGINEER — PROVINCE OF BRITISH COLUMBIA — B. R. DOLBEC # 57737

2025-11-03

REVISIONS	BY

TTF SCAFFOLDING Co. Ltd.
10979 OLSEN ROAD, SURREY, BC, V3V 3S9
TEL 778 899 5301
Email: info@ttfscaffolding.com
www.ttfscaffolding.com

JOB:
FRASER CRESCENT
32651 FRASER CRESCENT, MISSION, B.C.

CONTR:
HAMSTRA CONSTRUCTION LTD.

TITLE:
LEVEL 4 AND 5 SUSPENDED SLAB SHORING AND LEVEL 3 RESHORING PLAN FOR LEVEL 4 CONCRETE POUR

Date: OCT.30.2025
Scales: AS SHOWN
Drawn by: F.T.
Job:
Sheet: F-5
