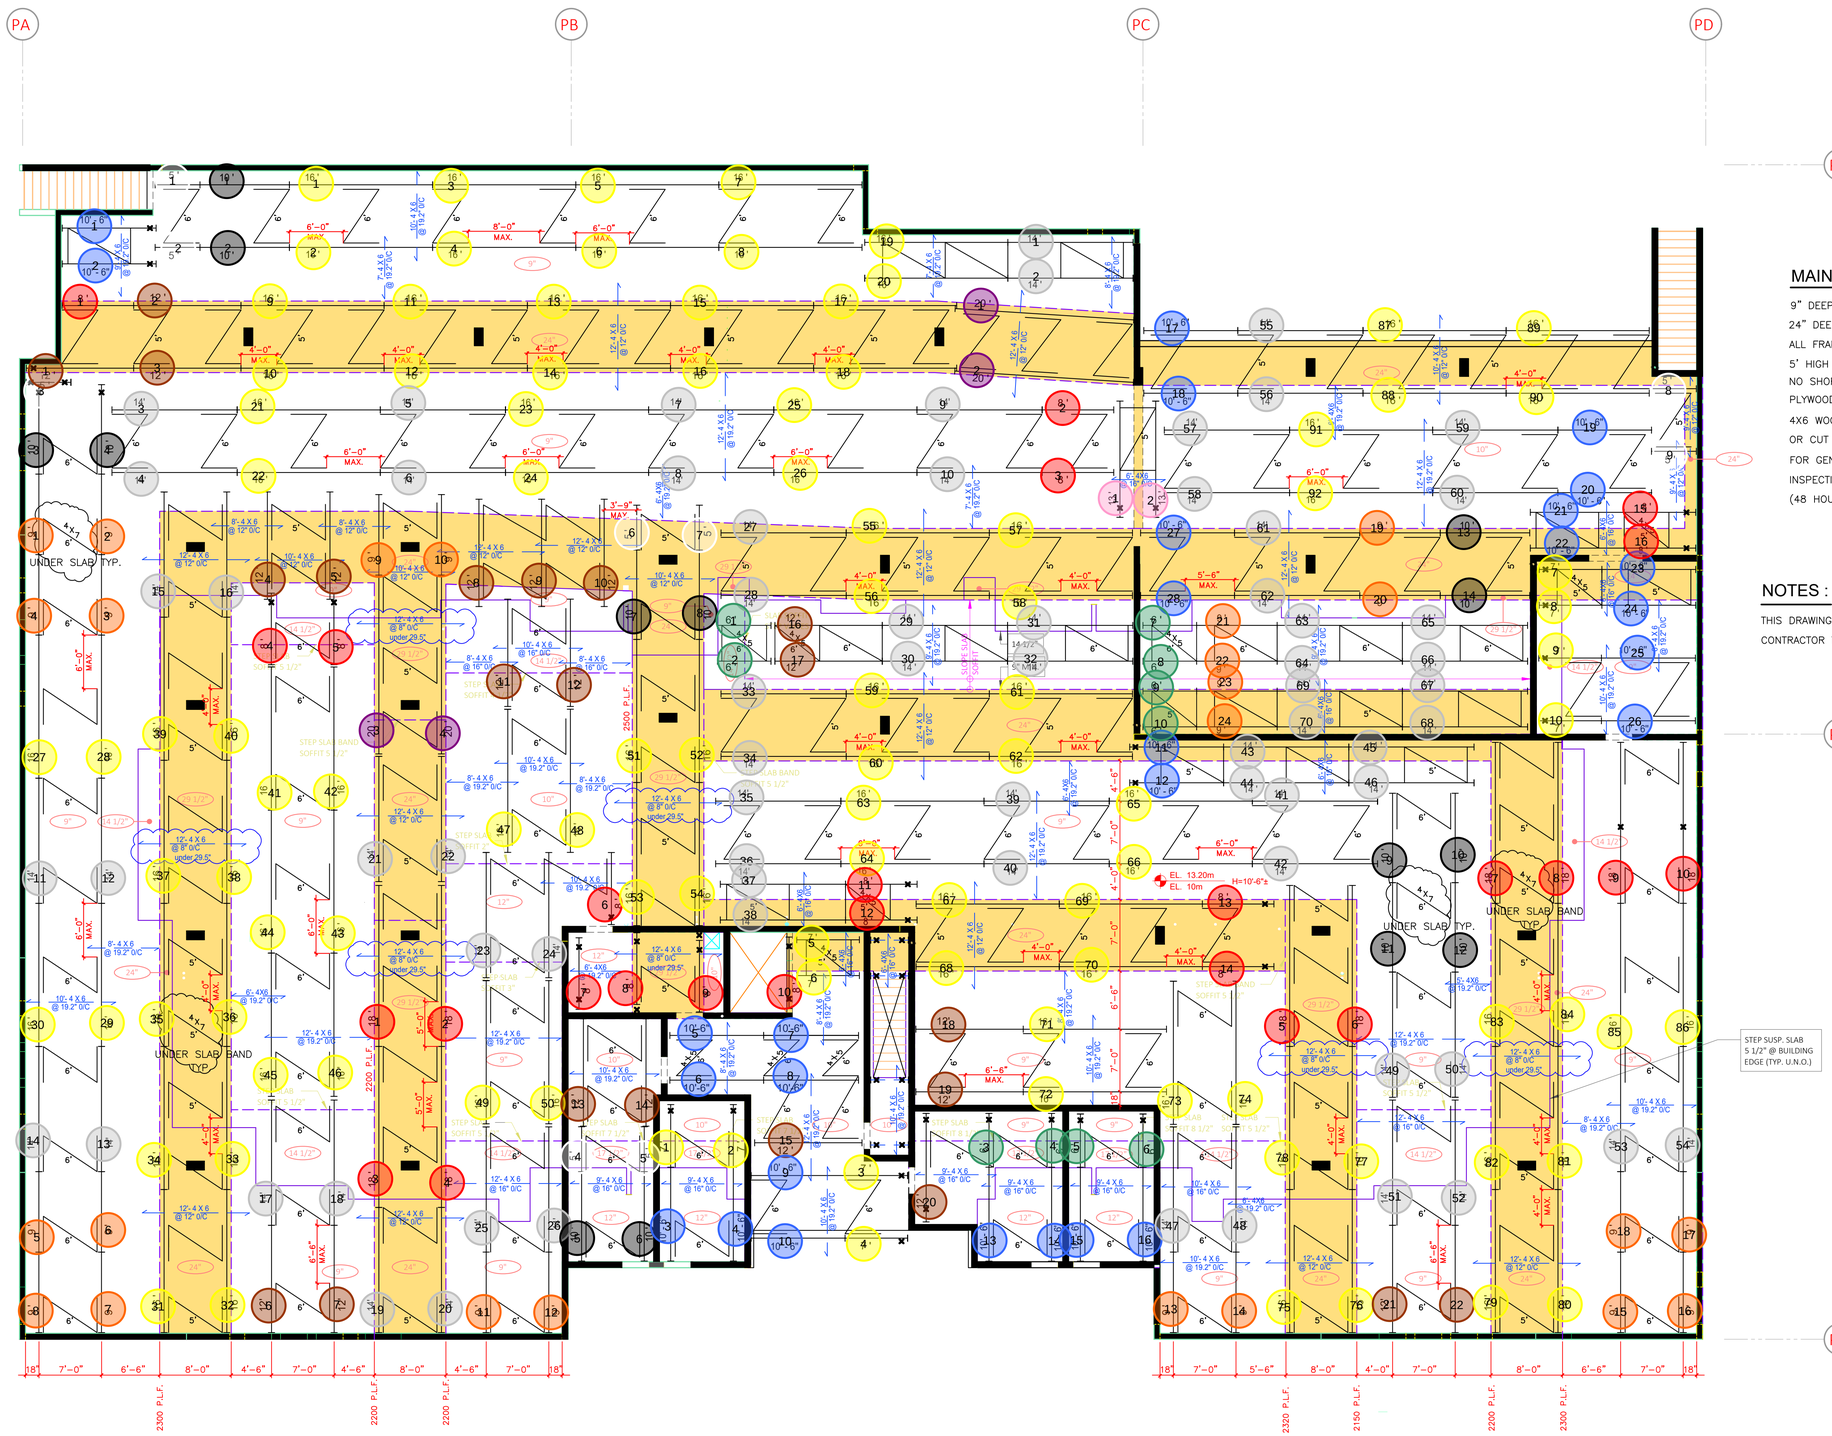


## MAIN FLOOR SUSPENDED SLAB SHORING PLAN: SCALE 1/8"=1'-0"

9" DEEP SLAB TYPICAL U.N.O. (163 P.S.F.)

24" DEEP SLAB BAND TYPICAL U.N.O. (350 P.S.F.)

ALL FRAMES TO BE 6' HIGH X 4' WIDE HEAVY DUTY(10 K/LEG) UNDER SLAB AND 5' HIGH X 4' WIDE UNDER SLAB BAND WITH 7'-0" BRACING TYP. U.N.O.

NO SHORE IS REQUIRED UNDER SLAB TYP. UNLESS SHOWN OR MARKED AS "✖" FOR #2 POST SHORE

PLYWOOD TO BE MIN. 3/4" D. FIR #1 OR BETTER.

4X6 WOOD JOISTS SUPPLIED BY TTF SCAFFOLDING SHALL NOT BE USED FOR PACKING OR CUT SHORT FOR OTHER PURPOSES.

FOR GENERAL NOTES AND TYPICAL DETAILS SEE DRAWING F-1.

INSPECTION IS REQUIRED BY UNDERSIGNED P.ENG. PRIOR TO POURING CONCRETE. (48 HOURS NOTICE PLEASE).

## NOTES :

THIS DRAWING SHALL BE READ IN CONJUNCTION WITH ARCHITECTURAL AND STRUCTURAL DRAWINGS.

CONTRACTOR TO CHECK AND CONFIRM ALL DIMENSIONS & ELEVATIONS PRIOR TO SHIPMENT OF EQUIPMENT.

| REVISIONS | BY |
|---|---|
| | |
| | |
| | |
| | |
| | |


TTF SCAFFOLDING Co. Ltd.

10979 OLSEN ROAD, SURREY, BC, V3V 3S9
TEL 778 899 5301
Email: info@ttfscaffolding.com
www.ttfscaffolding.com


**JOB:**

VESTA APARTMENT BUILDING

9345 CORBOULD STREET, CHILLIWACK, B.C.

**CONTR:**

OPEN DOOR CONSTRUCTION LTD.

**TITLE:**

MAIN FLOOR SUSPENDED SLAB SHORING PLAN & DETAILS

Date: MAY.12.2024

Scales: AS SHOWN

Drawn by: F.T.

Job:

Sheet: F-2
