1ST LEVEL NORTH SUSPENDED SLAB SHORING PLAN: SCALE 1/8"=1'-0"

8" DEEP SLAB TYPICAL U.N.O. (150 P.S.F.)
20" DEEP SLAB BAND TYPICAL U.N.O. (300 P.S.F.)
ALL FRAMES TO BE 4' WIDE HEAVY DUTY(10K/LEG) WITH 7' BRACING TYP.(SEE PLAN FOR FRAME HEIGHT).
NO SHORE IS REQUIRED UNDER SLAB NOR SLAB BAND TYP. UNLESS SHOWN OR MARKED AS "X" . (SEE PLAN FOR LOCATION).
PLYWOOD TO BE MIN. 3/4" D. FIR #1 OR BETTER.
4X6 WOOD JOISTS SUPPLIED BY TTF SCAFFOLDING SHALL NOT BE USED FOR PACKING OR CUT SHORT FOR OTHER PURPOSES.
FOR GENERAL NOTES AND TYPICAL DETAILS SEE DRAWING F-1.
INSPECTION IS REQUIRED BY UNDERSIGNED P. ENG. PRIOR TO POURING CONCRETE. (48 HOURS NOTICE PLEASE).

NOTES :

THIS DRAWING SHALL BE READ IN CONJUNCTION WITH ARCHITECTURAL AND STRUCTURAL DRAWINGS.
CONTRACTOR TO CHECK AND CONFIRM ALL DIMENSIONS & ELEVATIONS PRIOR TO SHIPMENT OF EQUIPMENT.

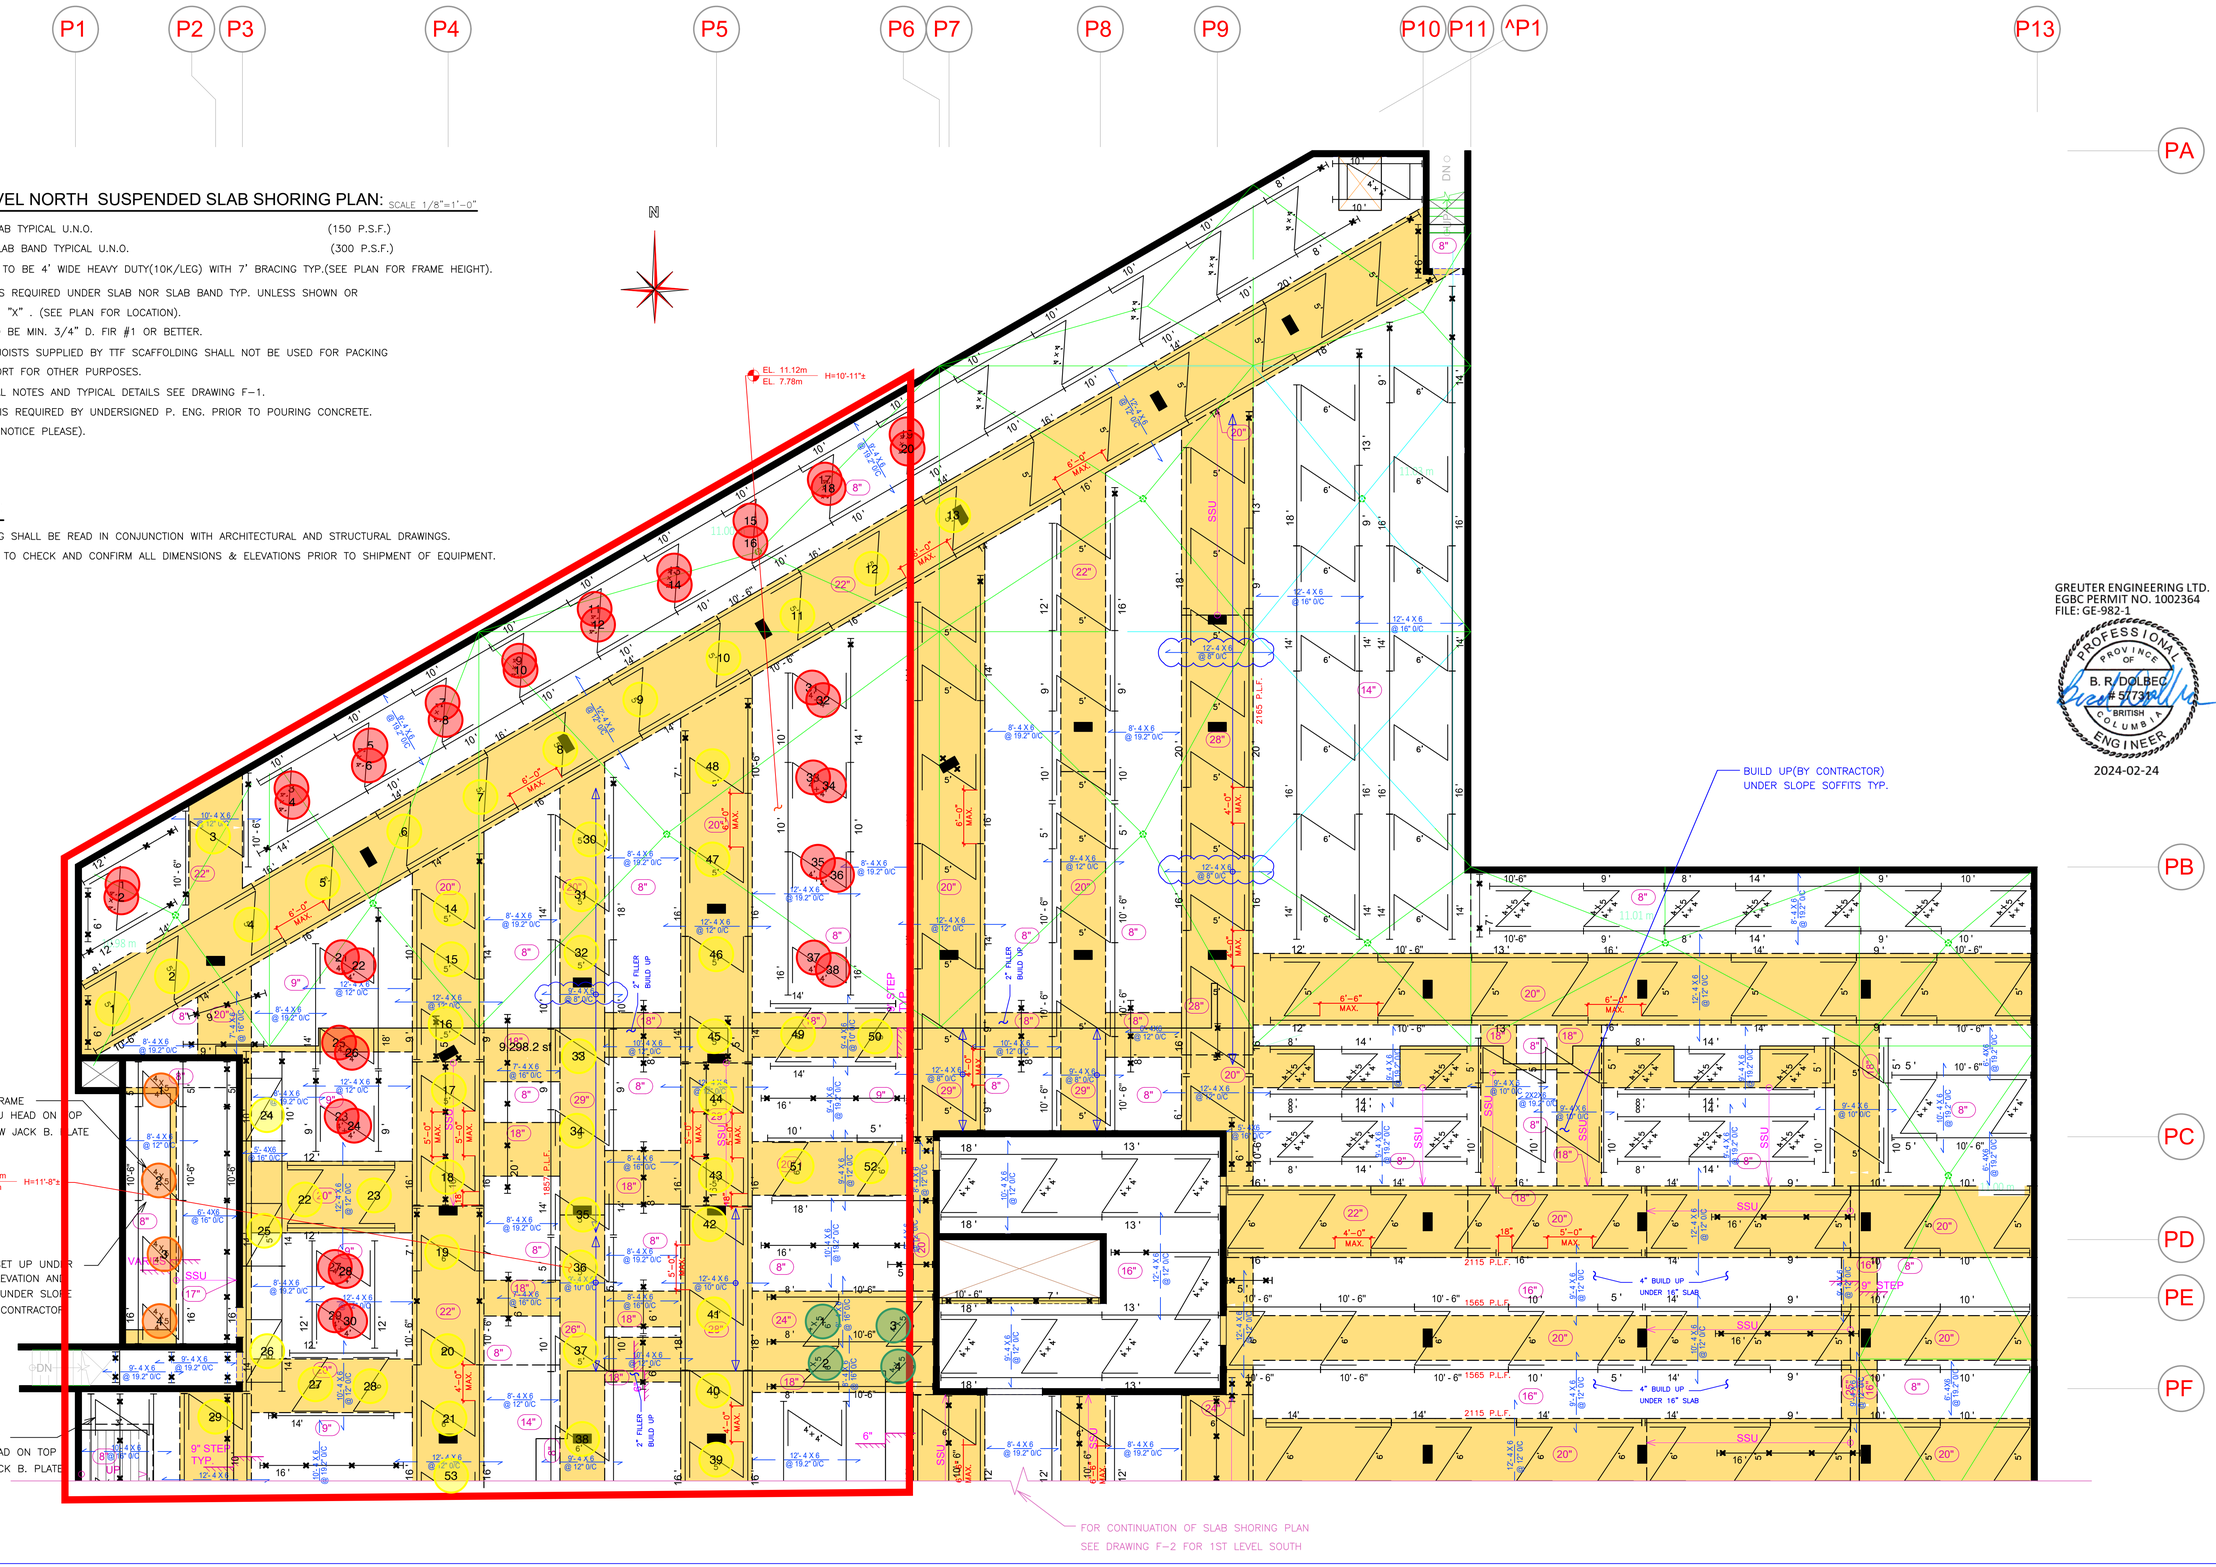

GREUTER ENGINEERING LTD.
EGBC PERMIT NO. 1002364
FILE: GE-982-1

PROFESSIONAL ENGINEER — PROVINCE OF BRITISH COLUMBIA — B. R. DOLBEC # 57737

2024-02-24

REVISIONS	BY

TTF SCAFFOLDING Co. Ltd.
10879 OLSEN ROAD, SURREY, BC, V3V 3S9
TEL. 778 898 5301
Email: info@ttfscaffolding.com
www.ttfscaffolding.com

JOB: THE HUDSON

5382 - 200 STREET, LANGLEY, B.C.

CONTR: 1100113 BC LTD.

TITLE: 1ST LEVEL NORTH SUSPENDED SLAB SHORING PLAN & DETAILS

Date: FEB.22.2024
Scales: AS SHOWN
Drawn by: F.T.
Job:
Sheet: F-3
