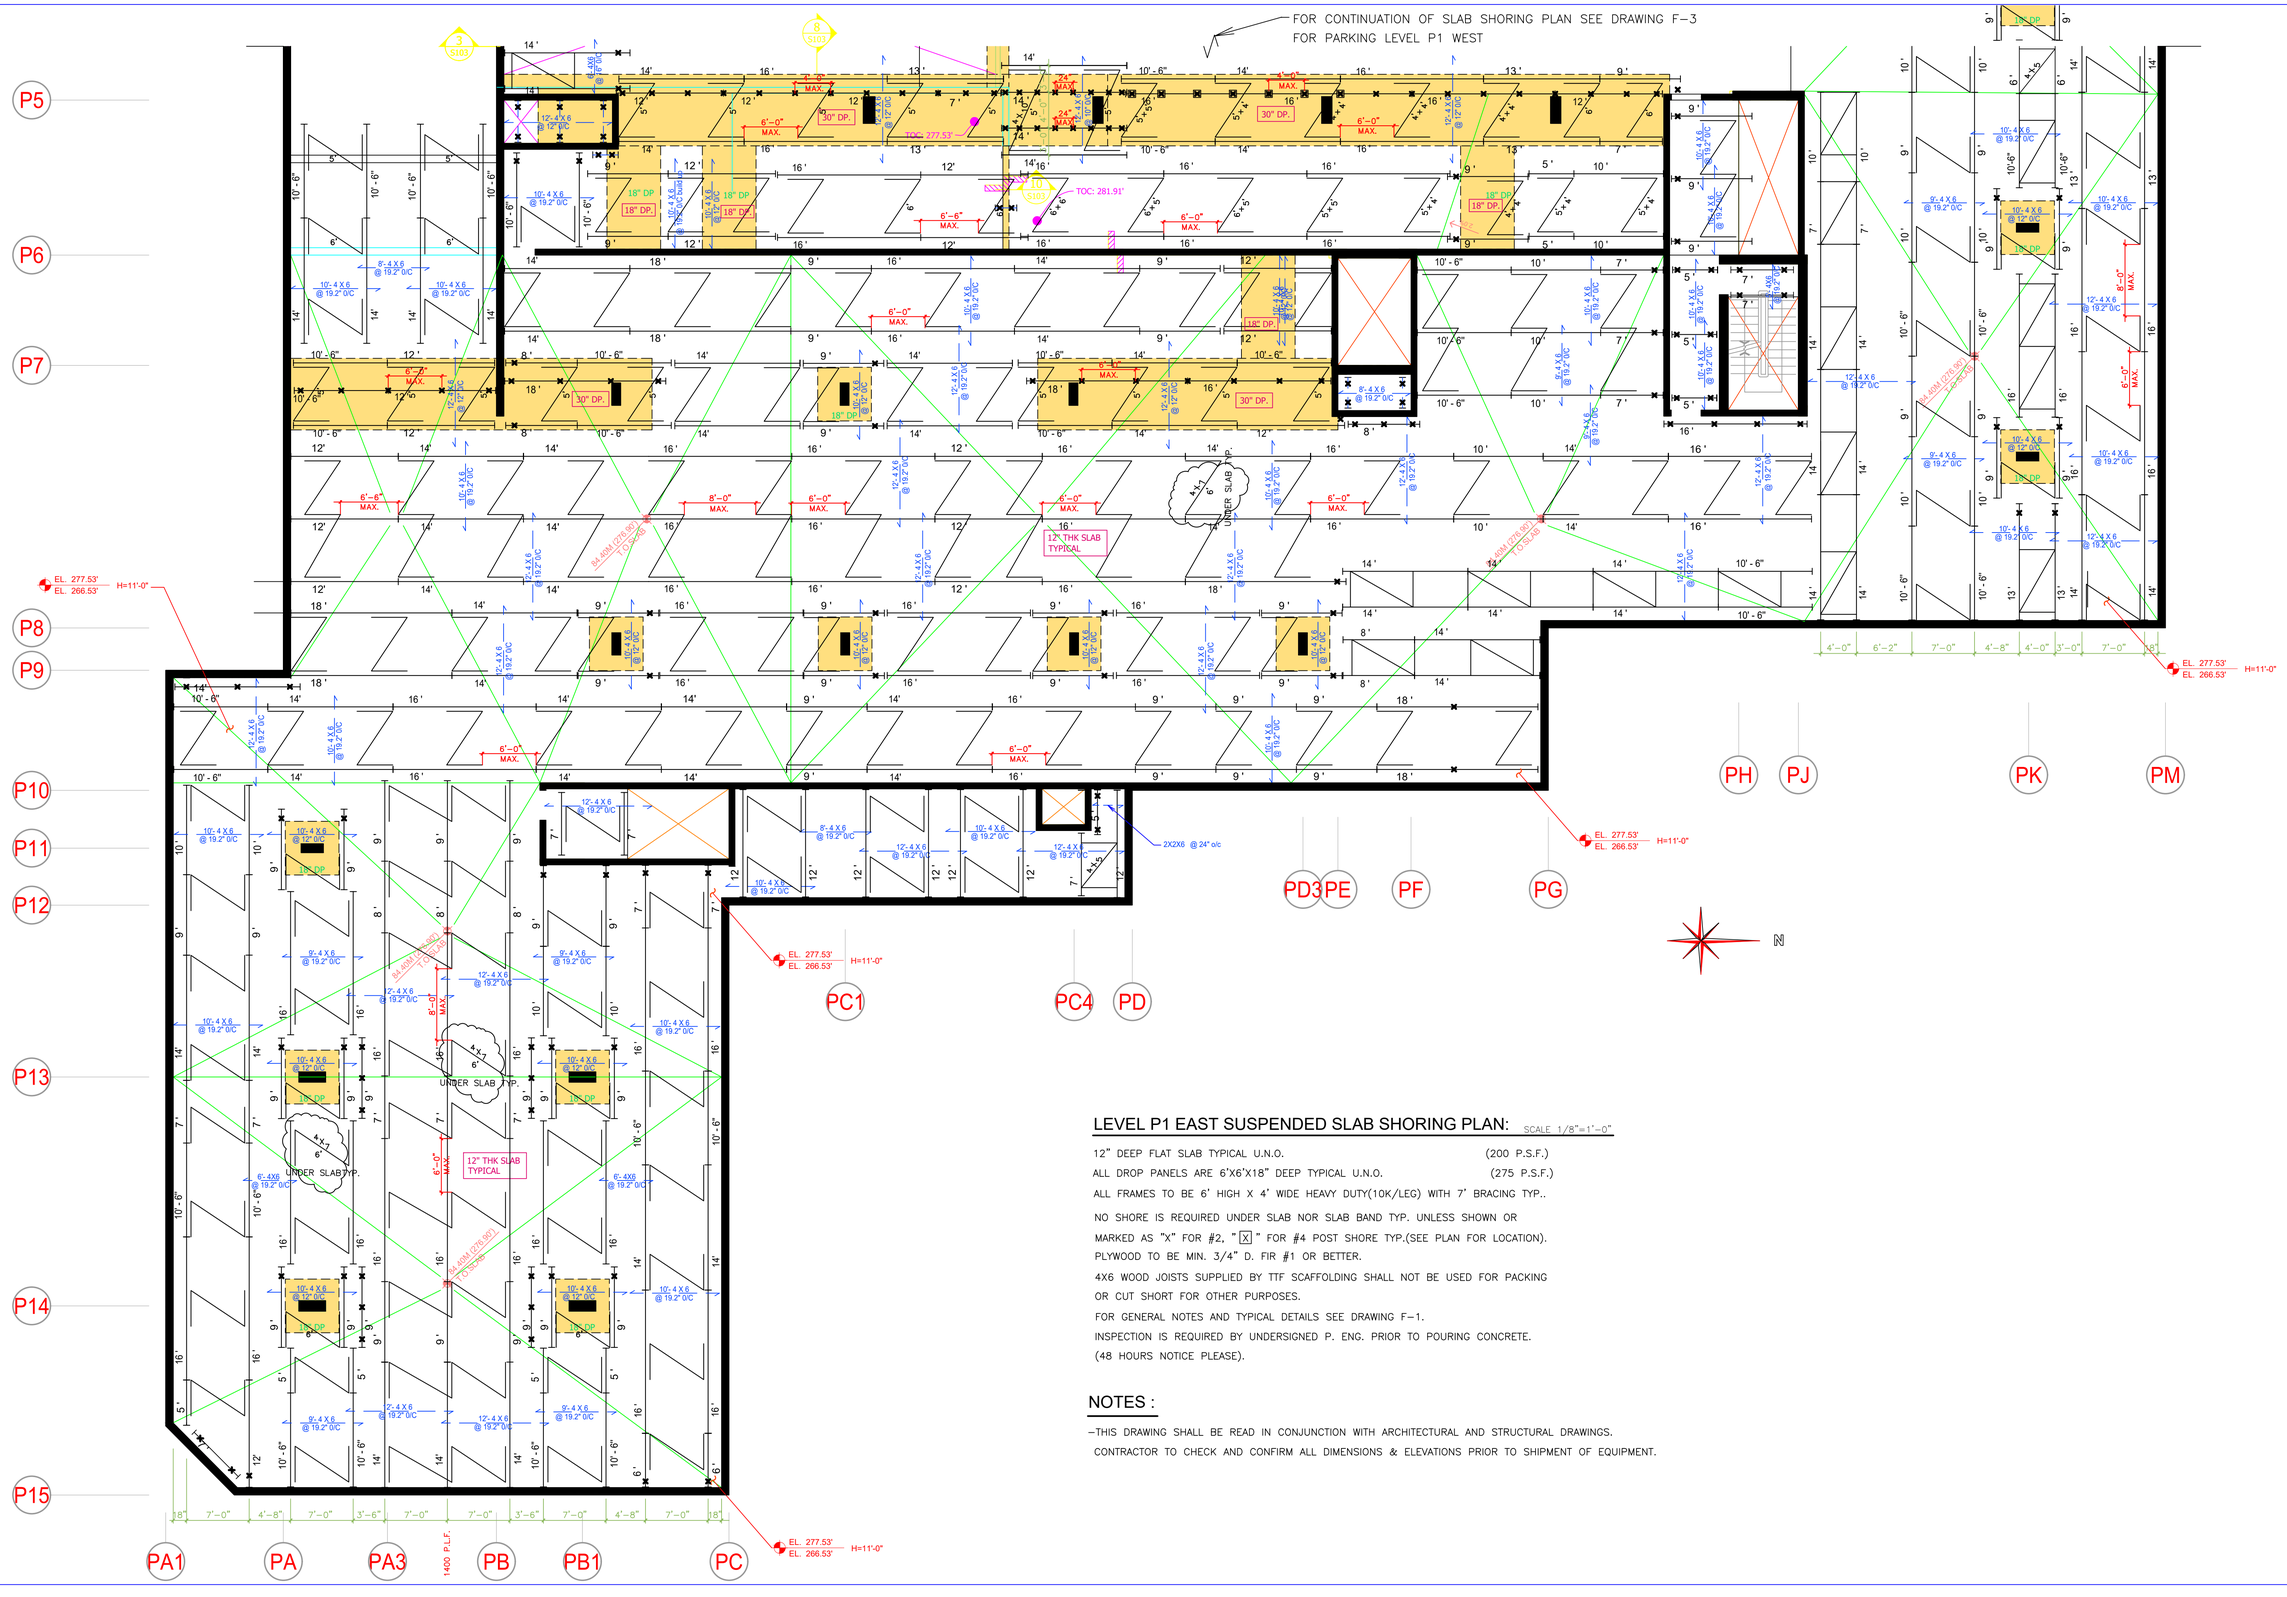

LEVEL P1 EAST SUSPENDED SLAB SHORING PLAN: SCALE 1/8"=1'-0"

12" DEEP FLAT SLAB TYPICAL U.N.O. (200 P.S.F.)

ALL DROP PANELS ARE 6'X6'X18" DEEP TYPICAL U.N.O. (275 P.S.F.)

ALL FRAMES TO BE 6' HIGH X 4' WIDE HEAVY DUTY(10K/LEG) WITH 7' BRACING TYP..

NO SHORE IS REQUIRED UNDER SLAB NOR SLAB BAND TYP. UNLESS SHOWN OR MARKED AS "X" FOR #2, "[X]" FOR #4 POST SHORE TYP.(SEE PLAN FOR LOCATION).

PLYWOOD TO BE MIN. 3/4" D. FIR #1 OR BETTER.

4X6 WOOD JOISTS SUPPLIED BY TTF SCAFFOLDING SHALL NOT BE USED FOR PACKING OR CUT SHORT FOR OTHER PURPOSES.

FOR GENERAL NOTES AND TYPICAL DETAILS SEE DRAWING F-1.

INSPECTION IS REQUIRED BY UNDERSIGNED P. ENG. PRIOR TO POURING CONCRETE. (48 HOURS NOTICE PLEASE).

NOTES :

-THIS DRAWING SHALL BE READ IN CONJUNCTION WITH ARCHITECTURAL AND STRUCTURAL DRAWINGS. CONTRACTOR TO CHECK AND CONFIRM ALL DIMENSIONS & ELEVATIONS PRIOR TO SHIPMENT OF EQUIPMENT.

REVISIONS	BY

TTF SCAFFOLDING Co. Ltd.
10979 OLSEN ROAD, SURREY, BC, V3V 3S9
TEL. 778 898 5301
Email: info@ttfscaffolding.com
www.ttfscaffolding.com

JOB:

TERRA GARDEN

15258 102A AVENUE, SURREY, B.C.

CONTR:

LEADING EDGE CONCRETE LTD.

TITLE:

LEVEL P1 EAST SUSPENDED SLAB SHORING PLAN & DETAILS

Date:	MAR.20.2024
Scales:	AS SHOWN
Drawn by:	F.T.
Job:	
Sheet:	F-2
